

Portland Harbor CAD Cell and Dredge Project: 2025-2026 Updates



Dredge and CAD Cell Overview





Winter 2025-2026 Dredge Summary

- Approximately 95,000 cubic yards of sediment dredged
 - 88,000 cy disposed of in the CAD Cell
 - 7,000 cy disposed of at PDS
- Approximately 9,700 linear feet of berthing improved along Portland's working waterfront.
- Four marinas and the South Portland City Pier dredged in South Portland





Before and After At Holyoke/Berlin Mills




Lots of Debris!







CAD Disposal and Floating Debris Management

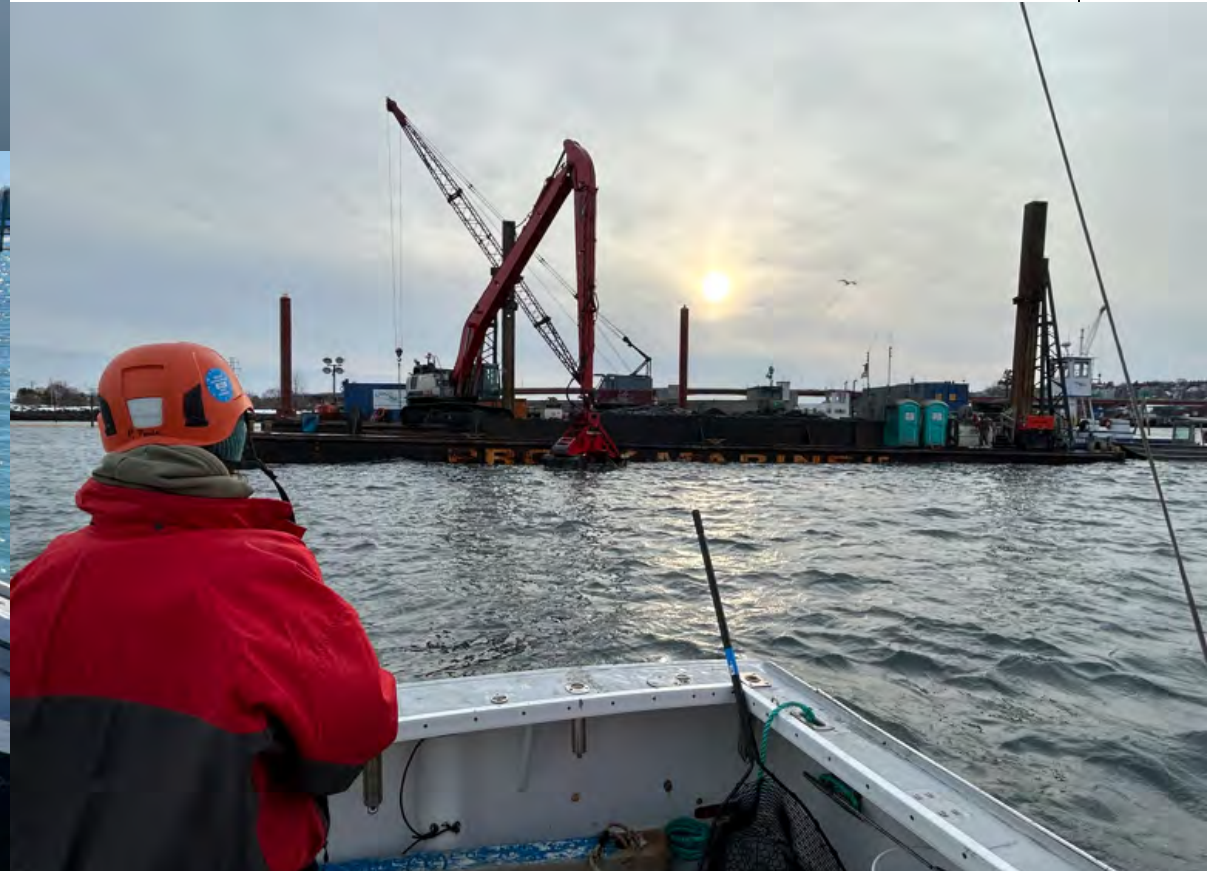



Winter 2026-2027 Dredge Planning

- Approximately 68,000 cubic yards of sediment to dredged
- Maine Yacht (permit update), Centerboard, East End Launch, Breakwater
- Approximately 142,000 cy of CAD Cell Capacity Remaining
- Approximately 88,000 cy of CAD Cell Capacity Prior to Berm
- June 2026 CAD Cell Survey to Confirm Capacity and Settling



Questions

